



Swansea Bay City Region Joint Committee - 10 November 2022

Financial Monitoring Report 2022/23 - Provisional Outturn Position Quarter 2

Purpose:	To provide Joint Committee with an update on the latest financial position of the Swansea Bay City Region.
Policy Framework:	Swansea Bay City Deal
Consultation:	Accountable Body
Recommendation(s):	It is recommended that the Joint Committee: 1) Review and approve the financial monitoring update report
Report Author:	Chris Moore
Finance Officer:	Chris Moore, Section 151 Officer, SBCD
Legal Officer:	Tracey Meredith, Monitoring Officer, SBCD

1. Introduction

1.1 This report details the forecasted year end outturn position of the Joint Committee and the Portfolio Investment Fund. The Financial Monitoring Report presents the City Deal Accounts in a detailed format, in line with Carmarthenshire County Council's financial management system.

2. Joint Committee – Estimated Forecast Outturn Position

2.1. Supplementary Information

The outturn position includes 'Top Slice' of Government Grants in terms of income. On drawdown of government grants, 1.5% of this will be utilised to support the PoMO and the direct administration functions of the Portfolio. Any contribution from Government grants utilised within the financial year will be transferred to a ring-fenced reserve at year end, for utilisation in future years.

A detailed breakdown of the Joint Committee financial outturn position is included in Appendix A.

2.2. Joint Committee and Accountable Body

The Joint Committee and Accountable Body expenditure forecast is estimated at £195k. This is in respect of democratic support, support of the portfolio monitoring officer and legal fees in respect of the funding agreements. Internal audit has been forecasted but is scheduled to be undertaken later within the financial year. The Accountable Body expenditure is attributable to service provision by the Portfolio Section 151 Officer to the Swansea Bay City Deal and the annual external audit review by Audit Wales.

The accrued interest in residual cash balances is invested inline with Carmarthenshire County Council's approved Treasury Management Strategy. Any interest accrued on such cash balances is dispersed back to projects on an appropriate apportionment methodology (JC – 11 June 2020). The accounting management of this has been amended to clearly demonstrate the interest accrued and paid out.

2.3. Joint Scrutiny Committee

The Joint Scrutiny Committee expenditure consists of democratic services and related costs, provided by Neath Port Talbot County Borough Council. This has been forecasted at £21k.

2.4. Portfolio Management Office (PoMO)

To the period ended 31st March 2023 the expenditure is estimated at £649k. The PoMO staffing cost is estimated at £497k, which includes an applied estimated inflationary adjustment. There is a small positive variance against budget, this is due to all posts being budgeted at the top of grade, savings due to in year temporary staffing vacancies and a small recharge in respect of the Finance Manager for work outside the SBCD.

Rents and service charges in respect of office space total £23k, fees including consultancy and gateway reviews have been forecast at £26k and conferences, marketing and advertising estimated at £39k including an SBCD annual event. ICT costs has been forecasted at £11k which includes project management software and associated training. Central Recharges of £26k has been included to contribute to Carmarthenshire County Council as the host Authority's costs for supporting the PoMO. These include payroll, Pensions, Creditors, Debtors, Human Resources support, Information Technology Support, financial systems support, Chief executive administration support, employee support and all necessary insurances.

2.5. Provision for Unwinding

This is an annual provision for the unwinding of the PMO at the end of its five-year operational requirement. Currently the total estimate is £152k, however it is demonstrated as 3/5th of an adjusted appointment (£99k) within the financial monitoring due to an accounting policy treatment.

2.6. Income

Total income for the year demonstrates £879k. This consists of partner contributions (£50k per partner) £400k, anticipated drawdown of 'Top Slice' of £449k from the dispersed grant awards and estimated interest derived from cash balances £30k.

2.7. Financial Monitoring - Statement of Balances

The prior year (2020/21) balance carried forward in reserve demonstrates £220k. Currently the estimated year end position of the City Deal accounts demonstrates a deficit of £84k, this is due to a timing effect attached to the grant dispersed to projects/programmes within the year. This concludes in an anticipated reserve of £136k at year end.

3. Portfolio Investment Fund – Forecast Outturn Position

Provisional Portfolio Investment Outturn Position


The overall estimated investment position is demonstrated at £1.248bn (Quarter 1 2021/22 - £1.239bn) over the fifteen-year life of the portfolio. The revised budget (Quarter 1 2022/23) comprised of a total investment of £1.246b, currently the City Deal is presenting a small over investment against the revised budget of £2m. Details of significant variances are outlined below:

Swansea Arena is currently demonstrating an underinvestment of £4m against budget due to the reappropriation of costs across the whole Copr Bay site. Work on final costs is still being undertaken and will be reported on in Quarter 2 in line with the amended programme being agreed with the contractor. The innovation matrix is currently demonstrating an over investment of £2m, which is being reviewed during quarter 3. A business case revision is currently being undertaken with a review of financials included.

Pentre Awel has commenced construction and is demonstrating £6m over investment against budget. Work is estimated to be completed during August 2024.

Prior Quarter Portfolio Forecasted Total (£m)	Investment Component	Revised Budget (Quarter 1) Total (£m)	Quarter 2 Portfolio Forecasted Total (£m)	Variance (£m)	Variance
235.70	City Deal	235.70	235.70	0.00	0.00%
373.50	Public	380.37	382.83	2.46	0.65%
629.61	Private	629.55	629.61	0.06	0.01%
1,238.81	Grand Total	1,245.61	1,248.14	2.53	0.20%

Prior Quarter Programme/Project Forecast Total (£m)	Programme/Projects	Quarter 2 Forecast				Revised Budget (Quarter 1) Total (£m)	Variance (£m)	Variance (%)
		City Deal Investment (£m)	Public Sector Investment (£m)	Private Sector Investment (£m)	Programme/Project Total (£m)			
55.00	Digital Infrastructure	25.00	13.50	16.50	55.00	55.00	0.00	0.00%
505.50	Homes as Power Stations	15.00	114.60	375.90	505.50	505.50	-	0.00%
135.01	LS&WB Campuses	15.00	58.58	62.01	135.59	134.95	0.64	0.47%
60.47	Pembroke Dock Marine	28.00	16.35	16.12	60.47	60.53	-0.06	-0.10%
200.18	Pentre Awel	40.00	57.99	108.19	206.18	200.48	5.69	2.84%
30.00	Skills & Talent	10.00	16.00	4.00	30.00	30.00	-	0.00%
59.08	Supporting Innovation and Low Carbon Growth	47.70	5.88	5.50	59.08	58.70	0.38	0.65%
168.40	Swansea Waterfront	50.00	81.25	39.90	171.15	175.28	-4.13	-2.36%
25.17	Yr Egin	5.00	18.67	1.50	25.17	25.17	-	0.00%
1,238.81	Grand Total	235.70	382.83	629.61	1,248.14	1,245.61	2.53	0.20%

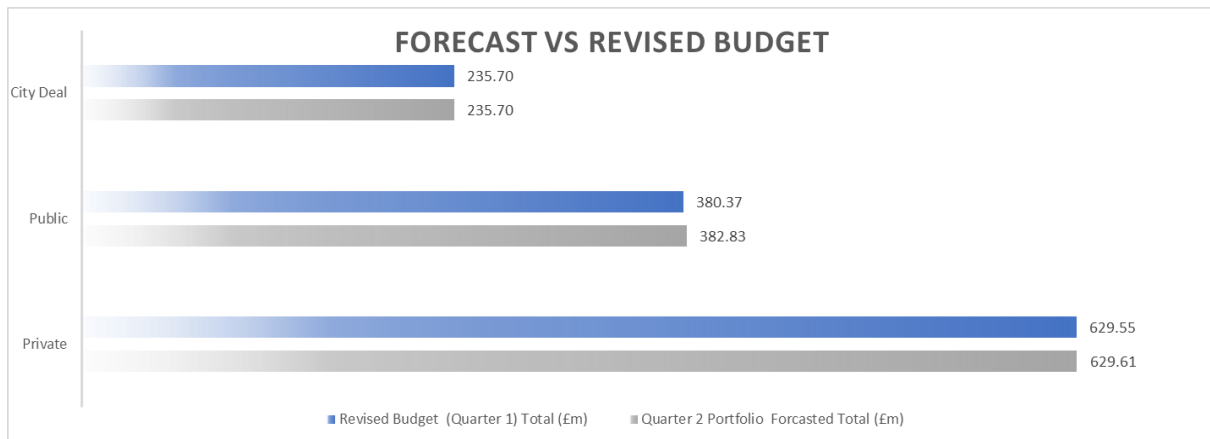

Provisional Annual Investment Forecast 2022/23

The forecast estimated investment for the financial year ended 31st March 2023 is demonstrated at £80m. The annual investment forecast is currently demonstrating an annual under-investment of £88m, in respect of the following:

The PDM project is continuing to review spend profiles on their public and private sector investment which could potentially affect the current year estimates. Currently the forecast was based on quarter four estimates, with a small slippage into the current financial year causing a slight over-investment. This is not expected to have an impact on the total investment.

Swansea Waterfront is demonstrating an in-year underinvestment due to accelerated City Deal spend in the previous year in respect of the arena, slippage in respect of private sector investment (including the hotel development) and slippage in project delivery in respect of the Innovation Matrix. This this is not expected to have an impact on the total investment for the programme.

Pentre Awel's annual investment profile was estimated as at quarter three, currently construction has commenced and will be completed as at August 2024. Whilst slippage has occurred this financial year due to small spend in the preliminary stages, this will accelerate over the remaining 17-month period of construction. This is not expected to have an impact on the total investment for the project.

The Skills and Talent project is demonstrating slippage in delivery within the year. The project has currently awarded funding to six successful school, further and higher education pilot projects and will review the funding mechanism in the new year. This this is not expected to have an impact on the total investment for the project.

Campuses is demonstrating a slippage in delivery due to the delay in engaging a funding agreement. issues have now been resolved and a funding agreement will be enacted imminently.

The SWITCH project is currently demonstrating slippage due to the delay of construction procurement and tendering, caused particularly by the COVID-19 pandemic but also as this project involves a close working relationship and

agreement with the delivery partner namely Swansea University. Unfortunately, the Swansea University Project Manager recently and there is ongoing dialogue with the new interim PM to agree on building requirements and specifications which caused the process to be drawn out over an extended period of 18 months. This is not expected to have an impact on the total investment for the project.

Digital infrastructure is currently demonstrating slippage within its rural project due to a “pause and review” which has been instigated for up to 3 months on the rural in-fill procurement, which has a planned spend of £6 million on Superfast broadband. This is due to an ongoing Open Market Review (OMR) being conducted by the Welsh Government and UK Government. The time will be spent liaising with Welsh and UK Governments on the outcome of the OMR, assessing the data and trying to better understand how far known private and public sector interventions are likely to go. This will support decision making in regards to whether investment is required and if so where investment should be directed from a commercial perspective. This will help to mitigate the risk of premises receiving double subsidy. It will also help to ensure we spend our funding in the most cost-effective way with maximum impact. There is anticipated capital slippage on connected places due to complications and delays associated to our regional collaborative procurement and slippage on Next Generation Wireless due to the capacity of the programme and its partners to deliver within this financial year. We will continue to update the regions Digital Infrastructure board on the evolving situation with future decisions brought back for discussion and authorisation. This is not expected to have an impact on the total investment for the project.

Portfolio Summary							
Prior Quarter Forecast Total	Description	Revised Budget	Quarter 2 Provisional Outturn Position				Variance
			Actuals (to Date)	Commitments	Forecast Commitments	Total Annual Forecast	
(£)		(£)	(£)	(£)	(£)	(£)	(£)
	City Deal Investment						
60,111,136	Capital	77,556,688	5,591,929	-	27,795,465	33,387,394	- 44,169,294
2,761,583	Revenue Expenditure (where capital receipts directive applied)	3,389,281	191,331	45,024	1,888,072	2,124,427	- 1,264,854
62,872,719	City Deal Total	80,945,969	5,783,260	45,024	29,683,537	35,511,821	- 45,434,148
	Public Sector Investment						
39,231,245	Capital	32,206,441	-	383,000	27,038,104	27,421,104	- 4,785,337
2,761,798	Revenue	5,840,485	-	-	2,761,798	2,761,798	- 3,078,687
41,993,043	Public Sector Total	38,046,926	-	383,000	29,799,902	30,182,902	- 7,864,024
	Private Sector Investment						
32,450,157	Capital	46,920,379	-	-	12,660,110	12,660,110	- 34,260,269
1,306,650	Revenue	1,306,650	77,286	-	1,229,364	1,306,650	-
33,756,807	Private Sector Total	48,227,029	77,286	-	13,889,474	13,966,760	- 34,260,269
	Project Total						
131,792,538	Capital	156,683,508	5,591,929	383,000	67,493,679	73,468,608	- 83,214,900
6,830,031	Revenue	10,536,415	268,617	45,024	5,879,233	6,192,875	- 4,343,541
138,622,569	Project Total	167,219,924	5,860,546	428,024	73,372,913	79,661,483	- 87,558,441

Annual Programme Investment Breakdown 2021/22 (Estimated)							
Prior Quarter Forecast Total	Description	Revised Budget	Quarter 2 Provisional Outturn Position				Variance
			Actuals (to Date)	Commitments	Forecast Commitments	Total Annual Forecast	
(£)		(£)	(£)	(£)	(£)	(£)	(£)
15,602,392	Digital Infrastructure	17,602,392	108,450	45,024	9,352,734	9,506,208	- 8,096,184
7,465,000	Homes as Power Stations	7,465,000	-	-	7,465,000	7,465,000	-
5,577,312	LS&WB Campuses	5,377,312	77,286	-	110,026	187,312	- 5,190,000
30,659,565	Pembroke Dock Marine	28,525,579	-	-	30,659,565	30,659,565	- 2,133,986
58,067,866	Pentre Awel	58,067,866	1,788,927	-	8,757,811	10,546,738	- 47,521,128
795,596	Skills & Talent	5,366,667	17,986	-	823,835	841,821	- 4,524,846
4,545,702	Supporting Innovation and Low Carbon Growth	11,769,275	-	383,000	4,162,702	4,545,702	- 7,223,573
15,909,137	Swansea Waterfront*	33,045,833	3,867,897	-	12,041,240	15,909,137	- 17,136,696
-	Yr Egin	-	-	-	-	-	-
138,622,569	Total	167,219,924	5,860,546	428,024	73,372,913	79,661,483	- 87,558,441

*budget as per business case

Capital and Revenue Apportionment

There is currently an estimated revenue requirement of £63m (5%) to deliver the city deal projects. This will be supported through the use of the Local Authorities flexible capital receipts directive, and alternative public and private sector commitment. The revenue requirement demonstrates a small change compared with the prior period (Quarter 1 2022/23 - £63m), this is as a result of some small fluctuation across several projects.

Capital/Revenue Summary (Estimated)

Investment Component	Capital Forecast (£m)	Revenue Forecast (£m)	Total Forecast (£m)	Revenue Proportion
City Deal	214.94	20.76	235.70	8.81%
Public	353.75	29.07	382.83	7.59%
Private	616.74	12.88	629.61	2.05%
Grand Total	1,185.43	62.71	1,248.14	5.02%

4. Financial Implications

- 4.1 The forecasted Joint Committee year end out-turn position (as at 31st March 2022) indicates a deficit of £84k, which will be supported by the Swansea Bay City Deal ring-fenced reserve at the year end. Expenditure is forecasted at £963k, which is offset by income through partner contributions of £400k and the 'Top Slice' of dispersed Government grants of £449k and interest income of £30k.
- 4.2 The business cases of all nine SBCD Portfolio programmes and projects have now been formally approved, a revised budget was compiled in quarter one for the portfolio demonstrating £1.246billion. The estimated portfolio forecasted investment position (as at 31st March 2022) demonstrates over investment against the revised budget of £2m. Currently the portfolio is presenting a total investment over the fifteen-year life span of the Swansea Bay City Region Deal of £1.248billion. This is subject to fluctuation over the life span of the project and will be monitored quarterly through financial templates and through the Portfolio risk register.


5. Legal Implications

- 5.1 There are no legal implications associated with this report.

Background papers: None

Appendices:

Appendix A – Provisional Outturn Position.

 Joint Committee - Provisional Outturn Position Financial Year 2022/23 <i>as at 30th September 2022</i>				
Description	Actuals 2021/22 (£)	Agreed Budget 2022/23 (£)	Forecast Outturn 2022/23 (£)	Variance (£)
Joint Committee and Accountable Body				
Room Hire	-	1,910	1,910	-
Subsistence & Meeting Expenses	-	3,496	-	3,496
Travel	-	-	-	-
Democratic Services - CCS	27,483	26,605	26,605	-
Monitoring Officer & Legal Services	35,659	36,640	36,640	-
External Legal Advisory Fees	-	25,000	-	25,000
Internal Audit Support	18,924	21,115	21,115	-
Staff Recruitment Expenses	-	-	-	-
External Audit Fees	14,971	25,000	21,830	3,170
Section 151 Officer	55,329	56,435	56,435	-
Interest paid over	39,575	-	30,000	(30,000)
Joint Committee and Accountable Body Total	191,942	196,201	194,535	1,666
Joint Scrutiny Committee				
Subsistence & Meeting Expenses	-	7,012	-	7,012
Travel	-	1,248	-	1,248
Democratic Services - NPT	21,332	21,226	21,226	-
Joint Scrutiny Committee Total	21,332	29,487	21,226	8,261
Portfolio Management Office				
Recharges - Employee Costs (direct)	461,842	552,056	496,990	55,065
Staff Recruitment Expenses	-	-	-	0
Training of Staff	1,220	26,530	5,000	21,530
Response Maintenance	-	-	-	0
Rents (The Beacon)	14,889	16,270	16,270	0
Rates (The Beacon)	6,688	7,184	7,184	0
Public Transport - Staff	-	2,081	1,300	781
Staff Travelling Expenses	76	16,646	5,493	11,153
Admin, Office & Operational Consumables	-	2,601	2,000	601
Furniture	-	1,000	1,000	0
Fees (including Gateway Reviews)	29,557	26,010	26,010	0
ICT Computer Hardware & Software	43	2,500	10,500	(8,000)
Subsistence & Meetings Expenses	10	8,323	3,000	5,323
Conferences, Marketing & Advertising	17,151	78,030	39,015	39,015
Projects & Activities Expenditure	-	14,566	-	14,566
Translation/Interpret Services	3,317	10,404	6,500	3,904
Printing & Copying	84	4,682	3,000	1,682
Photocopying Recharge	-	-	-	0
Central Recharge	-	-	25,512	(25,512)
Portfolio Management Office Total	534,876	768,883	648,775	120,108
Provision for Unwinding of PMO				
Redundancies	-	37,674	98,631	(60,957)
Provision for Unwinding Total	-	37,674	98,631	(60,957)
Total Expenditure	748,149	1,032,245	963,167	69,078
Funding Contributions				
Welsh Government - Revenue Grant	-	-	-	-
SBCD Grant Revenue Contribution	(314,119)	(723,000)	(449,196)	(273,804)
Partner Contributions	(400,000)	(400,000)	(400,000)	-
Interest Income	(39,575)	-	(30,000)	30,000
Total Income	(753,694)	(1,123,000)	(879,196)	(243,804)
Provision of Service - (Surplus) / Deficit	(5,545)	(90,755)	83,971	(174,726)
Movement to Reserves				
Description		2020/21 (£)	2021/22 (£)	
Balance Brought Forward from previous year - (Surplus) / Deficit		(214,816)	(220,361)	
Net Provision of Service - (Surplus) / Deficit		(5,545)	83,971	
Balance Carry Forward - (Surplus) / Deficit		(220,361)	(136,391)	
